ID	Task Name	Start	Finish	Duration
1	Regional Transmission Plan	5/19/2021	12/31/2021	163d
2	Technical Work: Develop and vet RCs; identify GIS needs	5/19/2021	5/26/2021	6d
3	Technical Work: Perform contingency analysis on RCs; determine if further IC combos are needed	5/27/2021	6/16/2021	15d
4	Report work: Initial Draft due	5/19/2021	6/22/2021	25d
5	Post Draft RTP for MPC Review	6/22/2021	6/22/2021	1d
6	MPC Review Draft report	6/23/2021	6/30/2021	6d
7	MPC Meeting to approve Draft RTP for stakeholder review	6/30/2021	6/30/2021	1d
8	Post Draft RTP for Stakeholder Review	6/30/2021	6/30/2021	1d
9	Stakeholder Comment Period on Draft report	6/30/2021	7/22/2021	17d
10	Stakeholder Meeting: present Draft report	7/7/2021	7/7/2021	1d
11	Report work: Summarize stakeholder feedback. Update report	7/23/2021	7/28/2021	4d
12	MPC Meeting: present stakeholder comments and any changes to Draft	7/28/2021	7/28/2021	1d
13	Technical Work: perform any additional analysis	7/28/2021	9/2/2021	26d 4h
14	Report Work: prepare Draft Final RTP for Member review	7/28/2021	9/21/2021	39d 4h
15	Post Draft Final RTP for MPC Review	9/21/2021	9/21/2021	1d
16	MPC Review of Draft Final report	9/22/2021	9/29/2021	6d
17	MPC Meeting to approve Draft Final for stakeholder review	9/29/2021	9/29/2021	1d
18	Post Draft Final RTP	9/29/2021	9/29/2021	1d
19	Stakeholder Comment Period	9/30/2021	10/21/2021	16d
20	Stakeholder Meeting: present Draft Final RTP	10/6/2021	10/7/2021	1d
21	Report work: Summarize Stakeholder feedback for Members	10/22/2021	10/27/2021	4d
22	MPC Meeting: present stakeholder comments and any changes to Draft	10/27/2021	10/27/2021	1d
23	Report work: finalize report	10/27/2021	12/1/2021	26d
24	Post RTP for MPC review	12/1/2021	12/1/2021	1d
25	MPC Review of RTP	12/1/2021	12/8/2021	6d
26	MPC Meeting to approve RTP	12/8/2021	12/8/2021	1d
27	Post RTP	12/9/2021	12/9/2021	1d

May 16 2021
May 23 2021
May 30 2021
Jun 6 2021
19
20
21
22
23
24
25
26
27
28
29
30
31
1
2
3
4
5
6
7
8
9
10
11
Technical Work: Develop and vet RCs; identify GIS needs
Technical Work: Perform contingency analysis on RCs; determine if further IC combos are
Report work: Initial Draft due

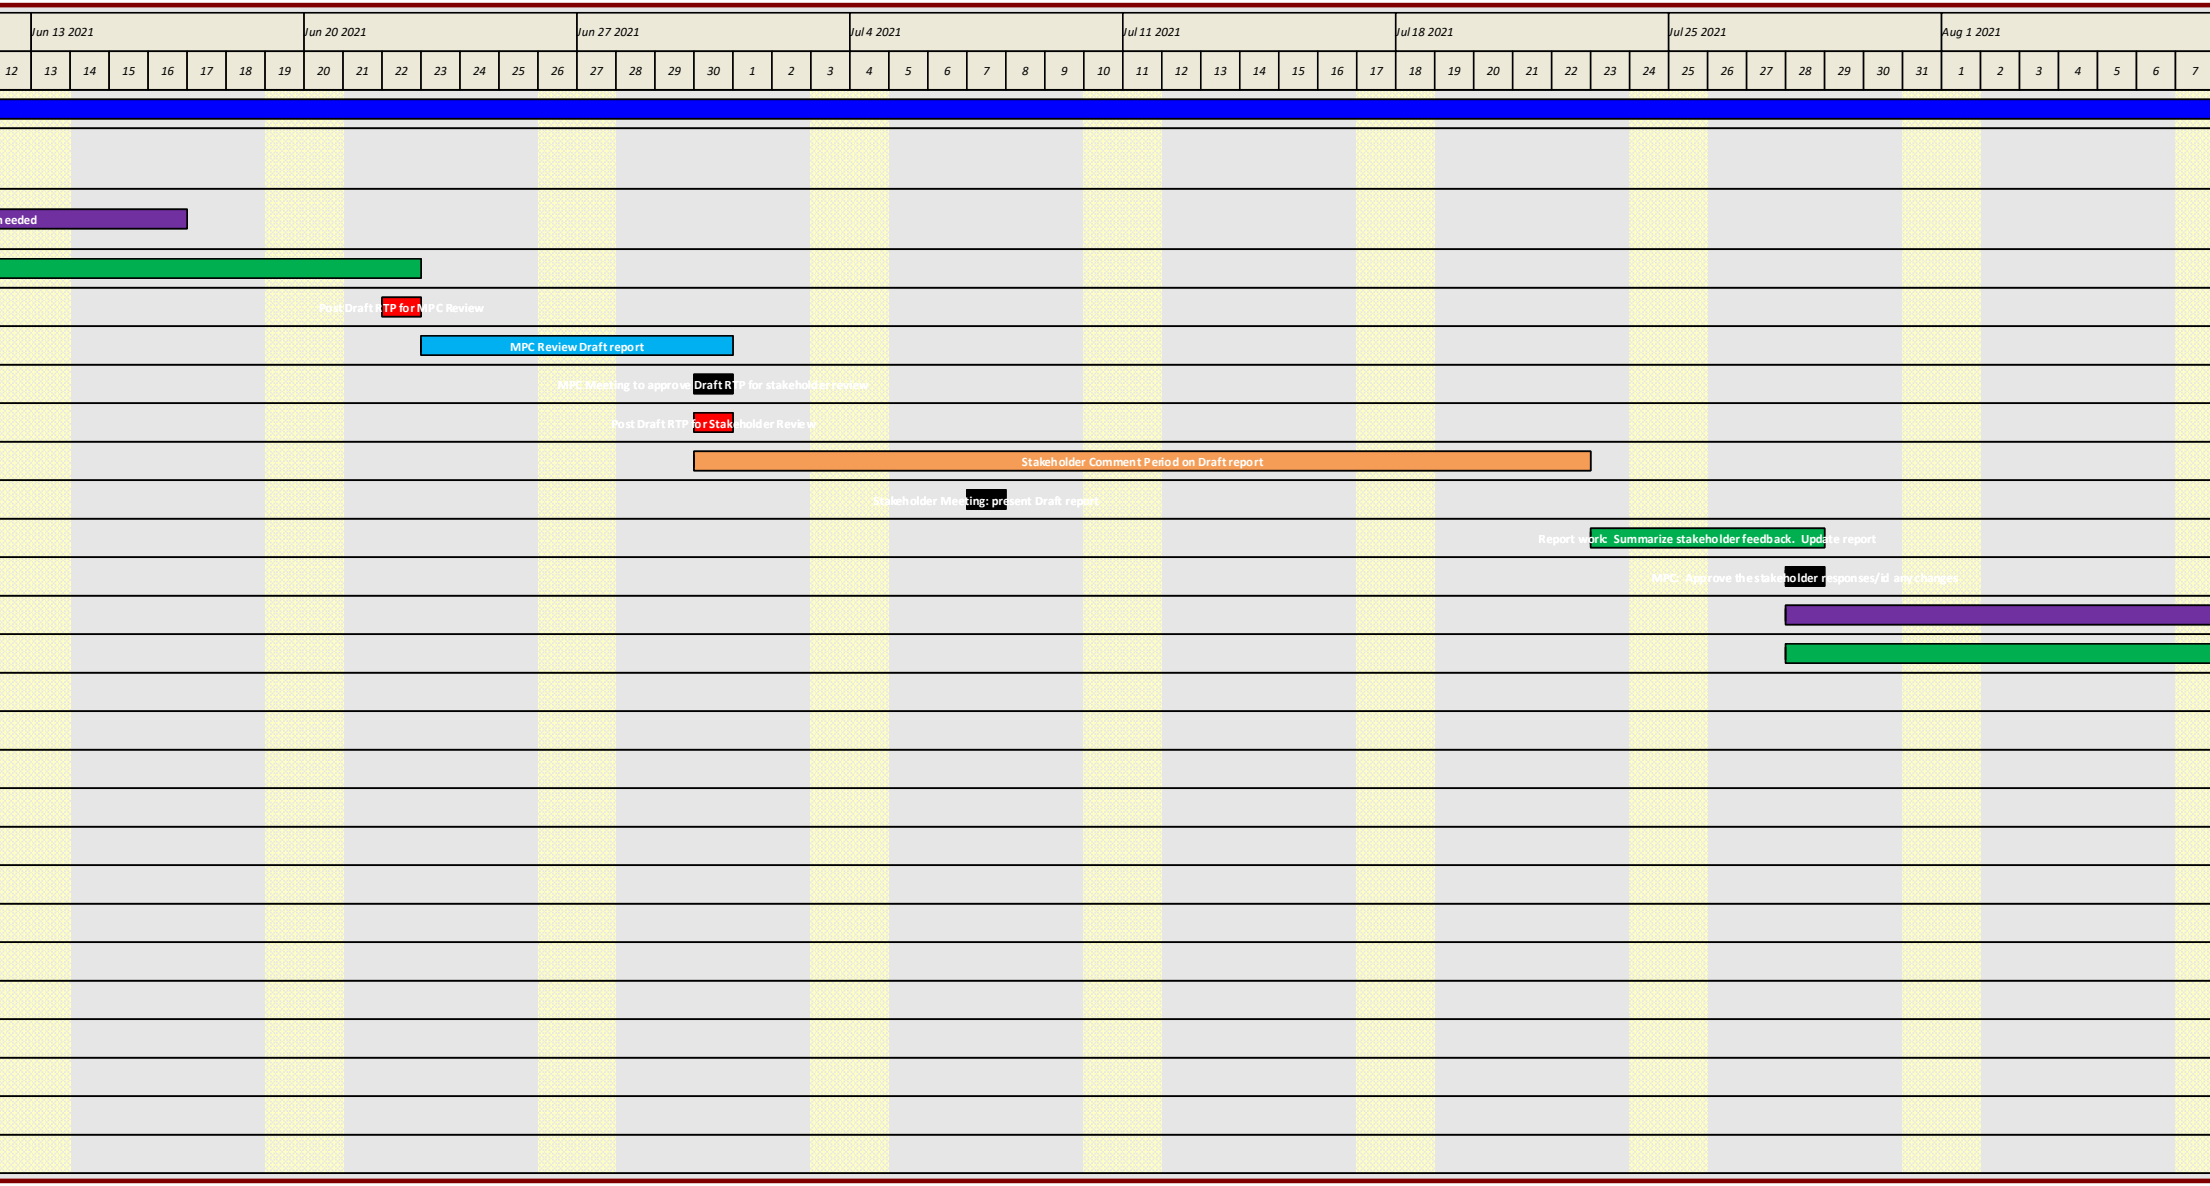

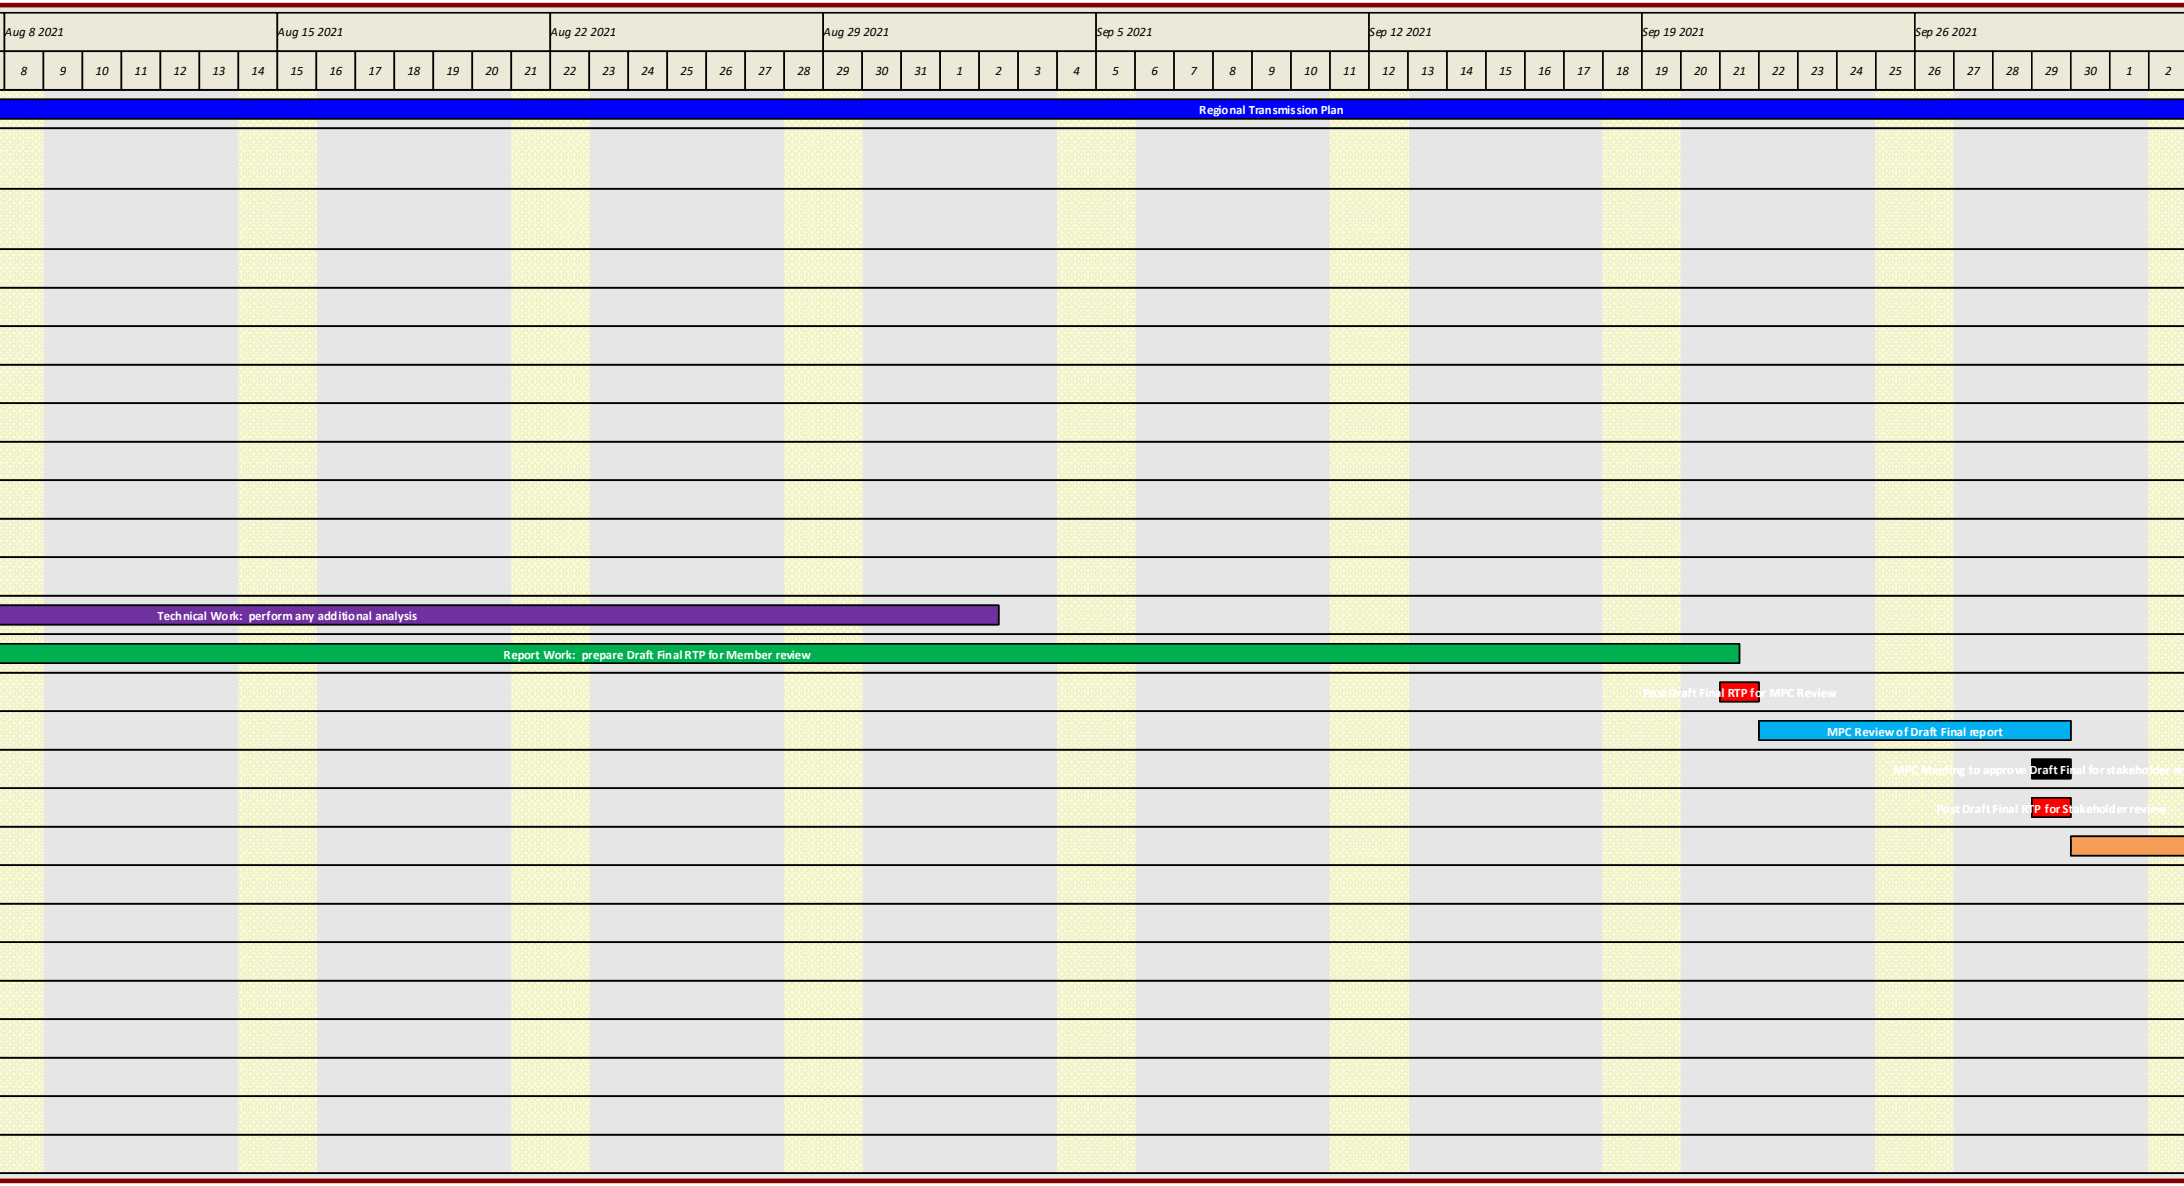

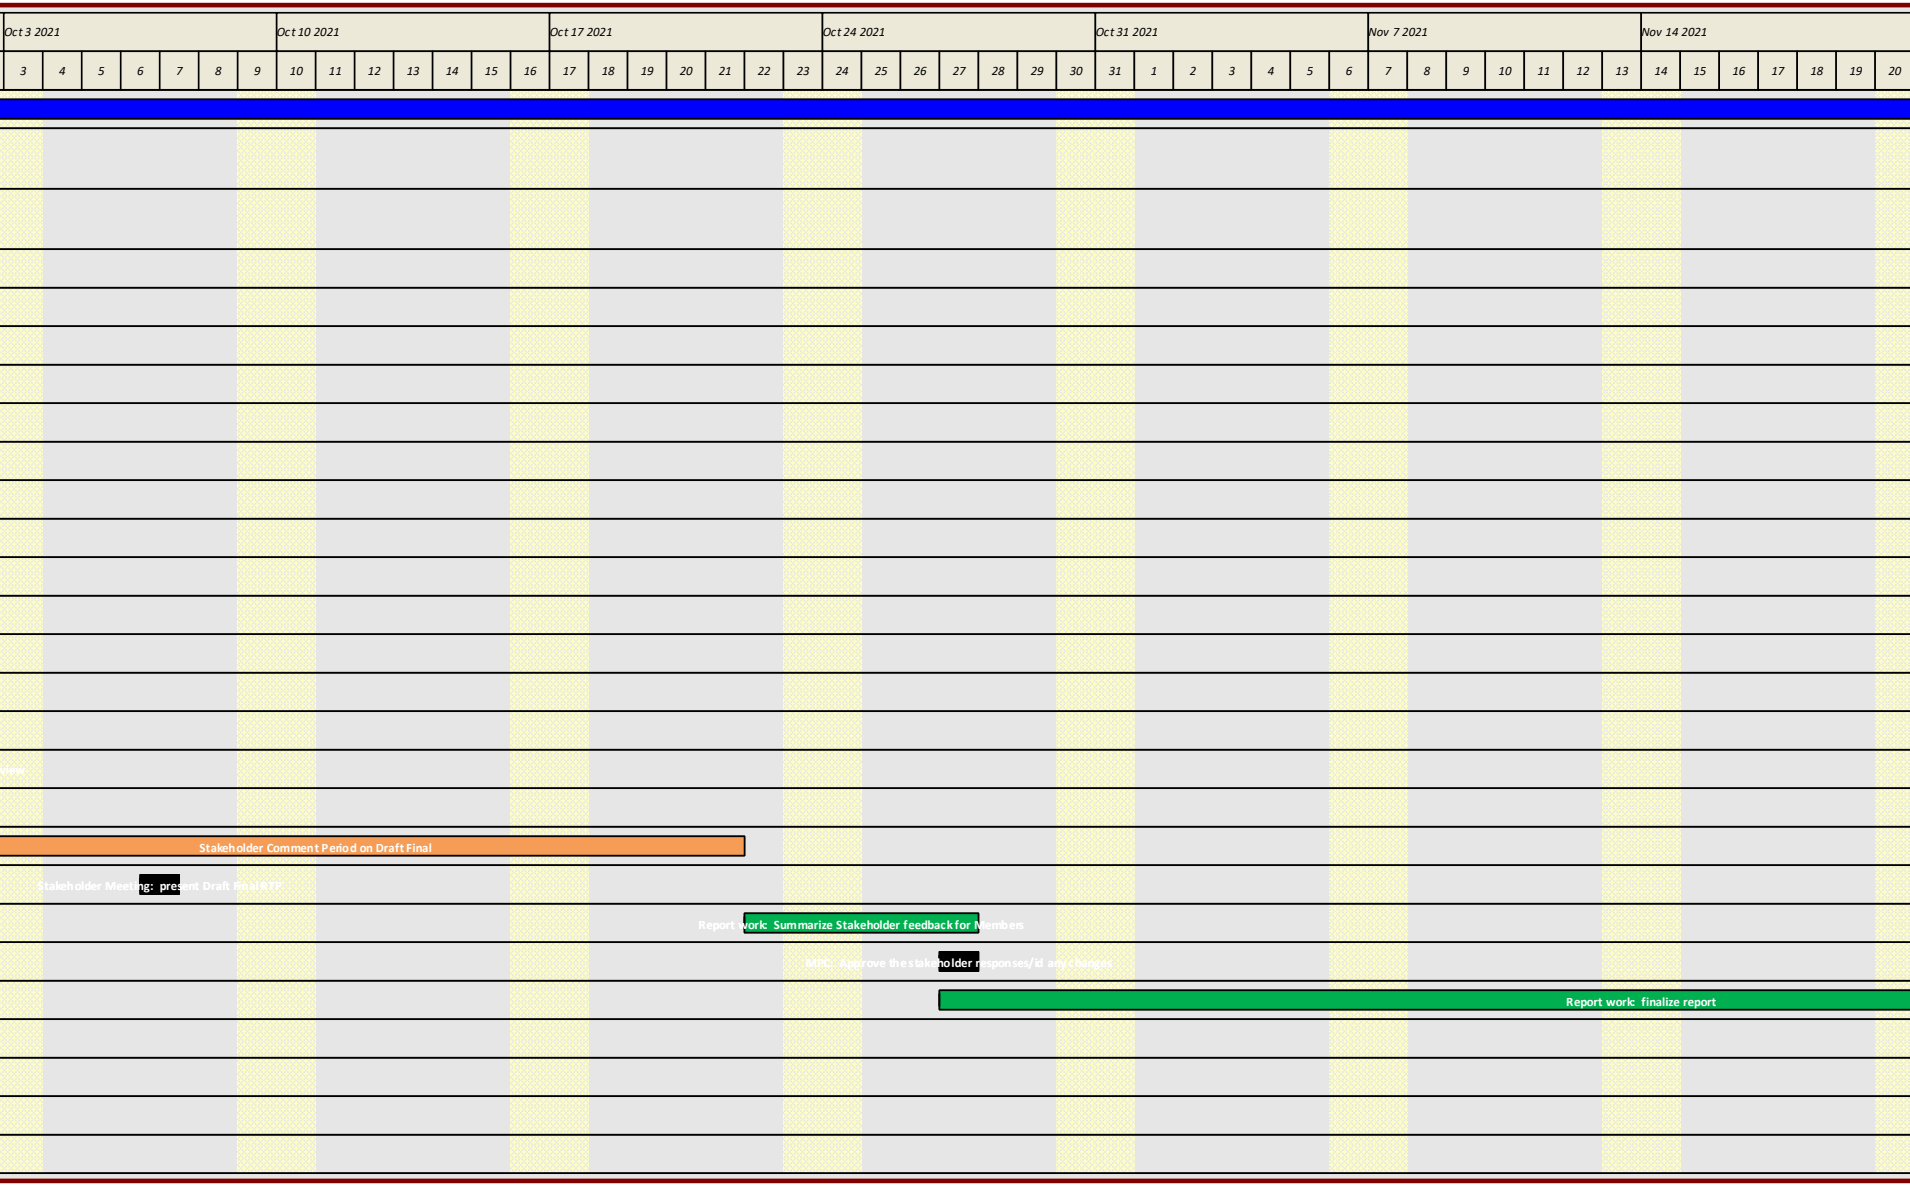

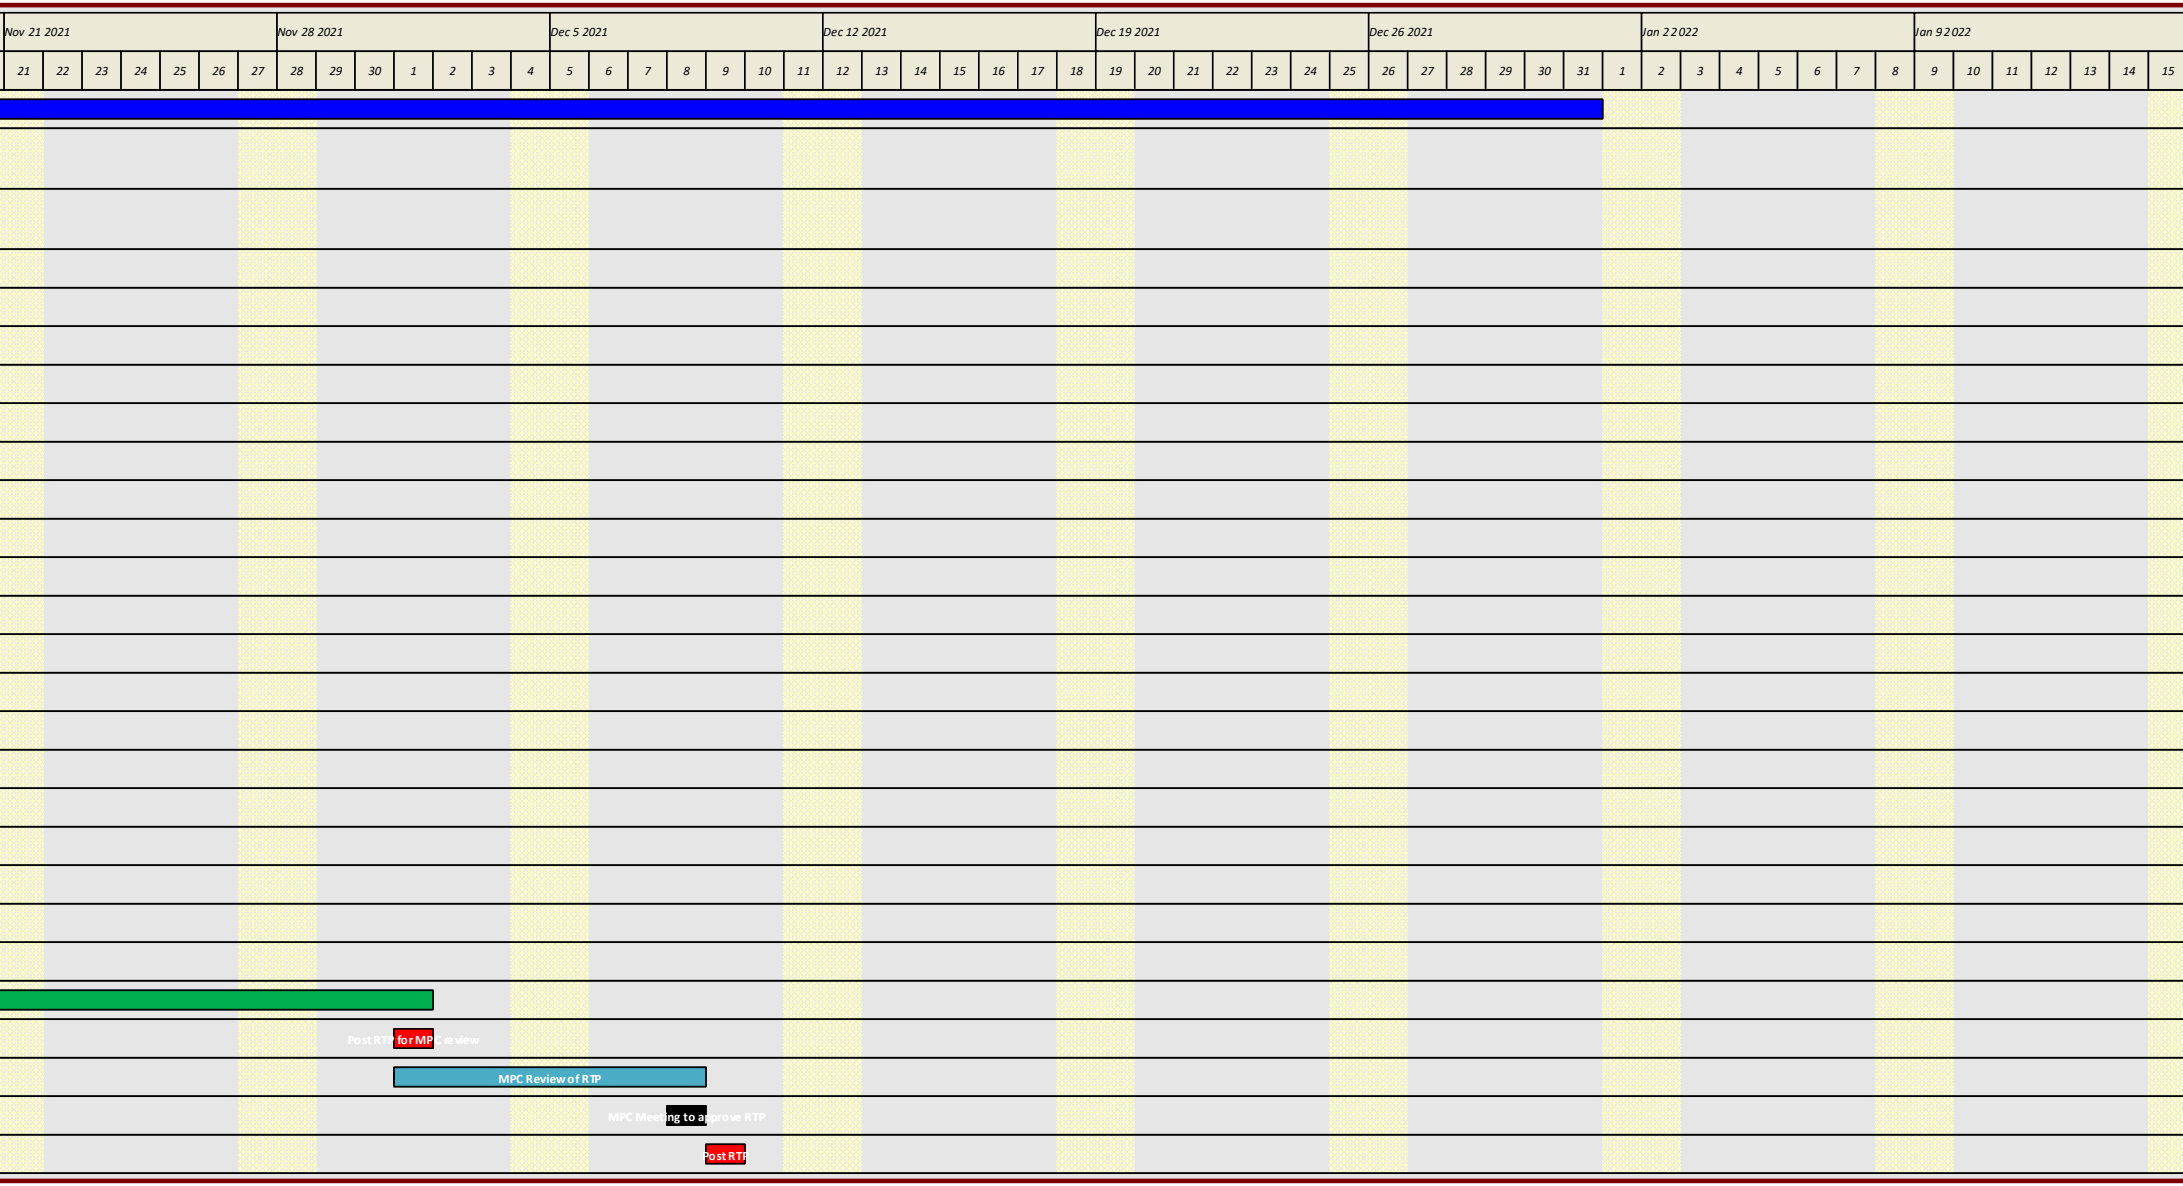

Jan 16 2022							Jan 23 2022							Jan 30 2022							Feb 6 2022							Feb 13 2022							Feb 20 2022							Feb 27 2022						
16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	1	2	3	4	5

Mar 6 2022							Mar 13 2022							Mar 20 2022							Mar 27 2022							Apr 3 2022							Apr 10 2022							Apr 17 2022							Apr 24 2022						
6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30

May 1 2022							May 8 2022							May 15 2022							May 22 2022							May 29 2022							Jun 5 2022							Jun 12 2022						
1	*2*	*3*	*4*	*5*	*6*	*7*	*8*	*9*	*10*	*11*	*12*	*13*	*14*	*15*	*16*	*17*	*18*	*19*	*20*	*21*	*22*	*23*	*24*	*25*	*26*	*27*	*28*	*29*	*30*	*31*	*1*	*2*	*3*	*4*	*5*	*6*	*7*	*8*	*9*	*10*	*11*	*12*	*13*	*14*	*15*	*16*	*17*	*18*

Jun 19 2022							Jun 26 2022							Jul 3 2022							Jul 10 2022							Jul 17 2022							Jul 24 2022							Jul 31 2022							Aug 7 2022						
19	20	21	22	23	24	25	26	27	28	29	30	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13

Aug 14 2022							Aug 21 2022							Aug 28 2022							Sep 4 2022							Sep 11 2022							Sep 18 2022							Sep 25 2022						
14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	1

Oct 2 2022							Oct 9 2022							Oct 16 2022							Oct 23 2022							Oct 30 2022							Nov 6 2022							Nov 13 2022							Nov 20 2022						
2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26

Nov 27 2022							Dec 4 2022							Dec 11 2022							Dec 18 2022							Dec 25 2022							Jan 1 2023							Jan 8 2023							Jan 15 2023						
27	28	29	30	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21

Jan 22 2023							Jan 29 2023							Feb 5 2023							Feb 12 2023							Feb 19 2023							Feb 26 2023							Mar 5 2023						
22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	1	2	3	4	5	6	7	8	9	10	11

Mar 12 2023							Mar 19 2023							Mar 26 2023							Apr 2 2023							Apr 9 2023							Apr 16 2023							Apr 23 2023						
12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29

Apr 30 2023							May 7 2023							May 14 2023							May 21 2023							May 28 2023							Jun 4 2023							Jun 11 2023	
30	*1*	*2*	*3*	*4*	*5*	*6*	*7*	*8*	*9*	*10*	*11*	*12*	*13*	*14*	*15*	*16*	*17*	*18*	*19*	*20*	*21*	*22*	*23*	*24*	*25*	*26*	*27*	*28*	*29*	*30*	*31*	*1*	*2*	*3*	*4*	*5*	*6*	*7*	*8*	*9*	*10*	*11*	*12*
